

Jira Sprint Evidence

Agile Project Management Submission

Name	B V Tejas
SRN	PES1UG24CS108
Section	B
Project	Household Carbon Footprint & Target Tracker
Jira board	https://tejasbhaskar14.atlassian.net/jira/software/projects/SCRUM/boards/1

Contents

1. Epics & User Stories (Product Backlog)
2. Story Points
3. Sprint History & Completion
4. Active Sprint Board
5. Burndown Charts
6. Reflection

1. Epics & User Stories (Product Backlog)

The backlog is organised under three epics that follow the product's dependency order: consumption data must be logged before reduction targets can be tracked, and coaching features build on both.

Epic	Title	Stories	Points
SCRUM-6	Consumption Logging & Carbon Calculation	3	10
SCRUM-7	Reduction Target & Progress Tracking	4	16
SCRUM-8	Sustainability Coaching & Collaboration	3	10

User stories

Key	User story	Epic	Pts	Status
SCRUM-9	Log Electricity & Transport Data	SCRUM-6	5	Done
SCRUM-10	Log Gas Consumption	SCRUM-6	3	Done
SCRUM-11	View Computed Monthly CO2e Total	SCRUM-6	2	Done
SCRUM-12	Set a Carbon Reduction Target	SCRUM-7	3	Done
SCRUM-13	Edit My Reduction Target	SCRUM-7	2	Done
SCRUM-14	View Historical Emissions Trend Chart	SCRUM-7	8	Done
SCRUM-15	Get Flagged When I Miss a Monthly Target	SCRUM-7	3	To Do
SCRUM-16	Coach Views Household Emission History	SCRUM-8	5	To Do
SCRUM-17	Coach Submits Recommendations	SCRUM-8	3	To Do
SCRUM-18	Resident Views Coach's Notes	SCRUM-8	2	To Do
	Total		36	

Spaces

Household Carbon Footprint & Target Tracker

Summary

Backlog

Board

Calendar

Timeline

Docs

Forms

Reports

SCRUM Sprint 3

25 Aug – 1 Sep (3 work items)

3

0

10

Complete sprint

Complete reduction target editing and historical emissions trend reporting, and begin monthly target miss alerts.

SCRUM-14

View Historical Emissions Trend Chart

Done

8

SCRUM-13

Edit My Reduction Target

Done

2

SCRUM-15

Get Flagged When I Miss a Monthly Target

To Do

3

+ Create

Backlog

(3 work items)

10

0

0

Create sprint

SCRUM-16

Coach Views Household Emission History

To Do

5

SCRUM-17

Coach Submits Recommendations

To Do

3

SCRUM-18

Resident Views Coach's Notes

To Do

2

+ Create

Jira Backlog view - Sprint 3 and remaining backlog, with epic tags and story points

2. Story Points

Estimation uses a modified Fibonacci scale (2, 3, 5, 8). Points reflect relative complexity rather than hours. All 10 stories are estimated; 36 points are planned in total, of which 23 are complete.

Scale	Meaning applied in this project	Stories
2	Small change to existing behaviour, no new data model	SCRUM-11, 13, 18
3	Single new form or rule, limited edge cases	SCRUM-10, 12, 15, 17
5	New data capture across multiple input types	SCRUM-9, 16
8	Aggregation plus visualisation; depends on prior data	SCRUM-14

Points delivered by epic

Epic	Planned	Delivered	Remaining
SCRUM-6 Consumption Logging	10	10	0
SCRUM-7 Reduction Target & Progress	16	13	3
SCRUM-8 Sustainability Coaching	10	0	10
Total	36	23	13

Spaces

Household Carbon Footprint & Target Tracker

Summary

Backlog

Board

Calendar

Timeline

Docs

Forms

Reports

SCRUM Sprint 3

25 Aug – 1 Sep (3 work items)

3010

Complete sprint

Complete reduction target editing and historical emissions trend reporting, and begin monthly target miss alerts.

SCRUM-14

View Historical Emissions Trend Chart

Done

8

SCRUM-13

Edit My Reduction Target

Done

2

SCRUM-15

Get Flagged When I Miss a Monthly Target

To Do

3

+ Create

Backlog

(3 work items)

1000

Create sprint

SCRUM-16

Coach Views Household Emission History

To Do

5

SCRUM-17

Coach Submits Recommendations

To Do

3

SCRUM-18

Resident Views Coach's Notes

To Do

2

+ Create

Story point badges visible on each work item row (Backlog view)

3. Sprint History & Completion

Two sprints have been formally completed in Jira. A third sprint is currently active. Figures below are taken directly from each sprint's burndown report.

Sprint	Status	Committed	Completed	Carried over	Rate
Sprint 1	Completed	19	8	11	42%
Sprint 2	Completed	18*	5	13	28%
Sprint 3	Active	13	10	3	77%

* Sprint 2 began with a 15-point commitment. SCRUM-15 (3 points) was added after the sprint started, raising the commitment to 18.

Sprint detail

Sprint	Completed in sprint	Carried into next sprint
Sprint 1	SCRUM-9 (5), SCRUM-10 (3)	SCRUM-12 (3), SCRUM-14 (8)
Sprint 2	SCRUM-12 (3), SCRUM-11 (2)	SCRUM-14 (8), SCRUM-13 (2), SCRUM-15 (3)
Sprint 3	SCRUM-13 (2), SCRUM-14 (8)	SCRUM-15 (3) - still open

Velocity. Measured velocity across the two completed sprints is 8 and 5 points, an average of 6.5 points per sprint. Sprint 3, scoped only to carried-over work, has delivered 10 of 13 points.

4. Active Sprint Board

Sprint 3 is the active sprint. Goal: *complete reduction target editing and historical emissions trend reporting, and begin monthly target miss alerts.*

Column	Work items	Points
To Do	SCRUM-15 Get Flagged When I Miss a Monthly Target	3
In Progress	-	0
Done	SCRUM-13 Edit My Reduction Target SCRUM-14 View Historical Emissions Trend Chart	10

Spaces

Household Carbon Footprint & Target Tracker

Summary

Backlog

Board

Calendar

Timeline

Docs

Forms

Reports

+

Complete sprint

To Do1

Get Flagged When I Miss a Monthly Target

Parent

Reduction Target & Progress Track... ▾

SCRUM-153=

+ Create

In Progress0

+ Create

Done2

View Historical Emissions Trend Chart

Parent

Reduction Target & Progress Track... ▾

SCRUM-148✓↗

Edit My Reduction Target

Parent

Reduction Target & Progress Track... ▾

SCRUM-132✓↘


+ Create

Active Sprint Board - Sprint 3, To Do / In Progress / Done

5. Burndown Charts

Burndown reports for the two completed sprints. The red line is remaining work; the grey line is the ideal burn rate.

Sprint 1 - 19 points committed, 8 delivered

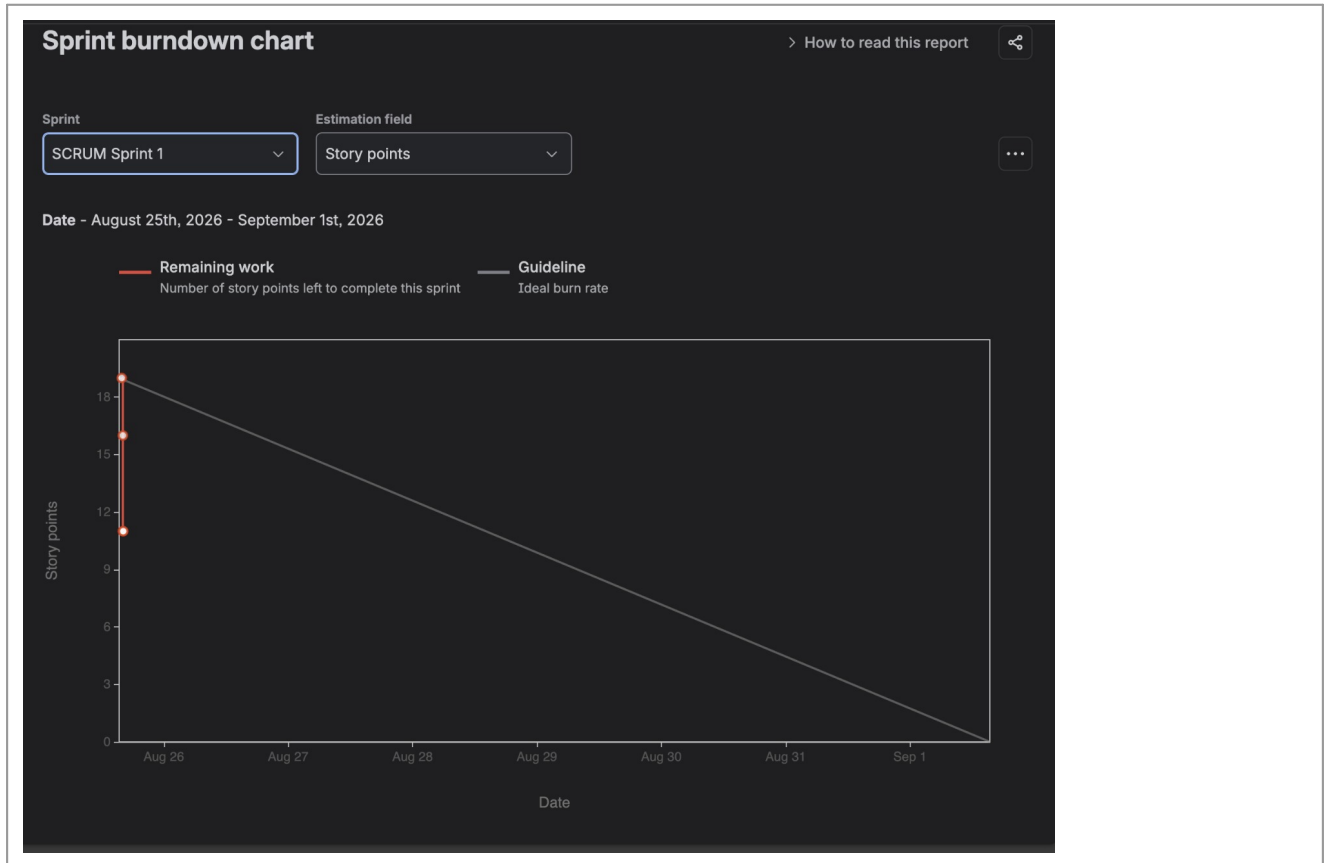

Burndown chart: SCRUM Sprint 1

Sprint 2 - 18 points committed, 5 delivered

Sprint burndown chart

> [How to read this report](#)



Sprint

SCRUM Sprint 2



Estimation field

Story points




Date - August 25th, 2026 - September 1st, 2026

Sprint goal - Continue reducing household carbon footprint by shipping reduction target tracking and remaining consumption logging features.

Remaining work
Number of story points left to complete this sprint

Guideline
Ideal burn rate

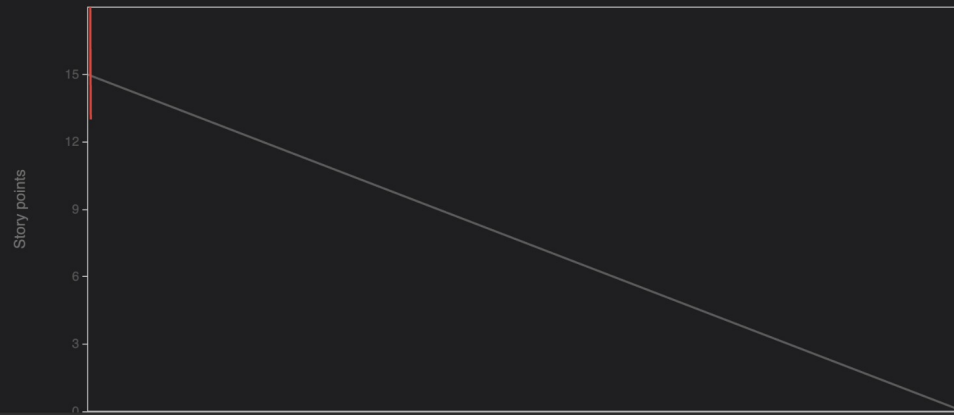

Burndown chart: SCRUM Sprint 2

6. Reflection

1. Did your estimations reflect the actual effort?

Partly. The small stories were estimated well: SCRUM-10 (3), SCRUM-11 (2), SCRUM-12 (3) and SCRUM-13 (2) each finished inside the first sprint in which they were seriously worked on. The estimate that did not hold was SCRUM-14, *View Historical Emissions Trend Chart*, at 8 points. It was pulled into Sprint 1, carried into Sprint 2, and was only finished in Sprint 3 - it spanned three sprints.

The 8 correctly identified it as the largest item, but it captured complexity only, not readiness. Charting a historical trend depends on several months of logged consumption data already existing, so the story had an upstream dependency on SCRUM-9, 10 and 11 that the number could not express. The lesson is that a high estimate on a dependent story is a signal to split it - data aggregation separately from chart rendering - or to hold it back until its dependencies close, rather than committing it alongside the very stories it depends on.

2. Was your backlog well-prioritized?

At epic level, yes. Sequencing *Consumption Logging* (SCRUM-6) ahead of *Reduction Target & Progress Tracking* (SCRUM-7) was right, because progress against a target cannot be shown without logged data, and leaving *Sustainability Coaching* (SCRUM-8) until last was right because it builds on both. That ordering held throughout and all 10 points of Epic SCRUM-6 are now delivered.

Within sprints the discipline was weaker. Sprint 2 opened already carrying 11 points of unfinished work, and SCRUM-15 was then added mid-sprint, raising the commitment from 15 to 18. Two small stories were closed while the highest-value blocked item, SCRUM-14, slipped for a second time. The priority order was sound; the work-in-progress discipline was not. Carried-over work should have been finished before anything new was admitted.

3. How did your simulated sprint align with your plan?

Alignment improved sharply once the plan became realistic. Sprints 1 and 2 planned 19 and 18 points and delivered 8 and 5 - roughly a third of what was committed each time. Sprint 3 was deliberately scoped to carried-over work only: 13 points, no new stories, no mid-sprint additions. It delivered 10 of 13, or 77%.

SCRUM-15 remains open, so Sprint 3 is not fully complete, but that is a realistic result and far closer to plan than either earlier sprint. The pattern is clear: alignment improved exactly when the commitment was cut toward observed capacity and the scope was frozen for the duration of the sprint.

4. What insights did the burndown chart give about your team's capacity?

The charts show consistent over-commitment. Measured velocity was 8 points and then 5 points, an average of 6.5 per sprint, against commitments of 19 and 18 - roughly two and a half to three times actual capacity. Sprint 3's 13-point commitment with 10 delivered is much closer to sustainable.

A realistic planning figure going forward is 8 to 10 points per sprint. On that basis the 13 points still outstanding (SCRUM-15, 16, 17 and 18) represent roughly one and a half sprints of work, not one, which is the kind of forecast the burndown makes possible and guesswork does not.
